

Dashboard Insights Report


Analysis of Projects, Tasks, Milestones and HR Performance data underlying the Power BI dashboard



Executive Summary


- The portfolio holds **15 projects** worth a combined budget of **■2.45 Cr**, against actual spend of **■1.64 Cr** (-32.9% vs budget overall). Only **1 of 15 projects** is marked Completed; **7 are On Hold** and **2 are Cancelled**, leaving average completion at just **49%**.
- Of **189 tasks** tracked, **43 are Blocked** (the single largest status group), and **153 tasks are past their due date and still open**. **36 Critical-priority tasks** remain unresolved.
- Delivery discipline is under pressure at the milestone level too: of **65 milestones**, **19 (29%) are Delayed**, versus only **16 Achieved**.
- On the people side, average performance score is **3.65/5** and **16 of 60 reviews** recommend promotion. However, **14 employees are allocated over 100%** of capacity across active projects, a resourcing risk that likely contributes to the blocked-task and delayed-milestone volume above.

Project Status at a Glance

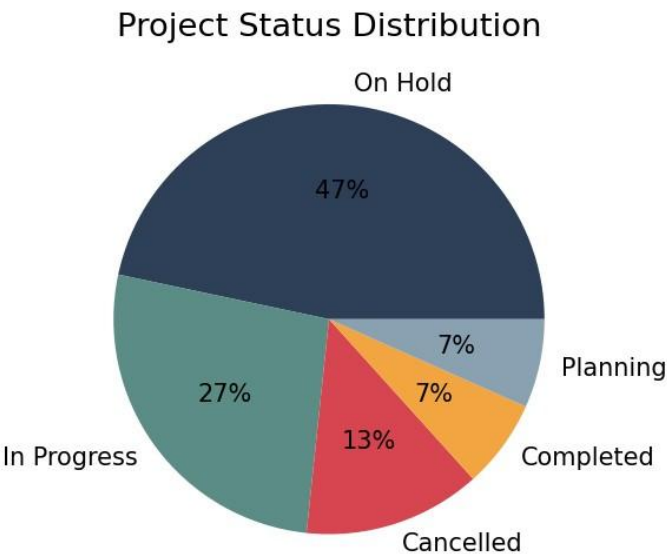

Project Portfolio

The portfolio spans nine categories, led by Digital Transformation (4 projects) and Marketing Campaign (3 projects). Despite an overall budget underspend of ■8.06 Cr (actual cost running below budget across 13 of 15 projects), this reflects stalled progress rather than efficiency — most underspent projects are also the ones On Hold, Cancelled, or still in Planning, so the funds are unspent because the work hasn't happened yet.

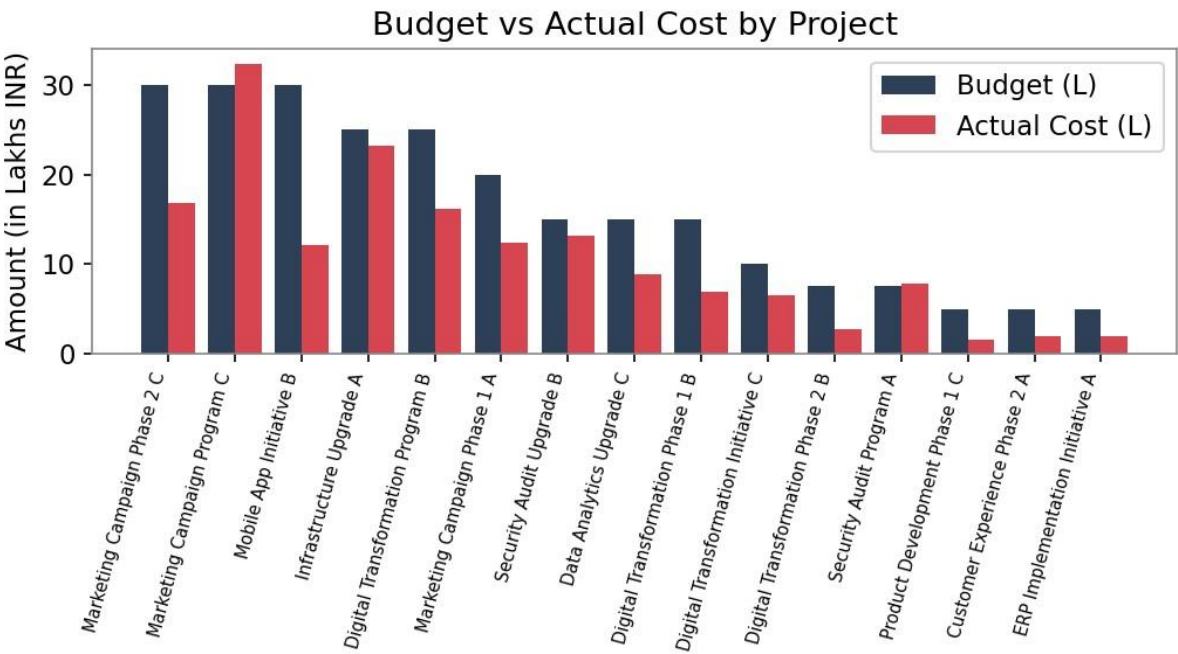


At-Risk / Stalled Projects (lowest completion %)

Project	Status	Priority	Completion	PM
Digital Transformation Phase 2 B	Cancelled	High	6%	Karan Mishra
Marketing Campaign Phase 2 C	In Progress	High	8%	Suresh Chauhan
Data Analytics Upgrade C	Planning	High	8%	Aarav Saxena
Security Audit Program A	On Hold	High	17%	Karan Rastogi
Security Audit Upgrade B	On Hold	High	26%	Sunita Agarwal
Customer Experience Phase 2 A	Cancelled	Medium	30%	Vikram Dubey


Two projects are running over their approved budget: **Marketing Campaign Program C** (+7.9%, though 95% complete — largely a true cost overrun) and **Security Audit Program A** (+5.1%, but only 17% complete — an early warning sign).

Task & Delivery Performance

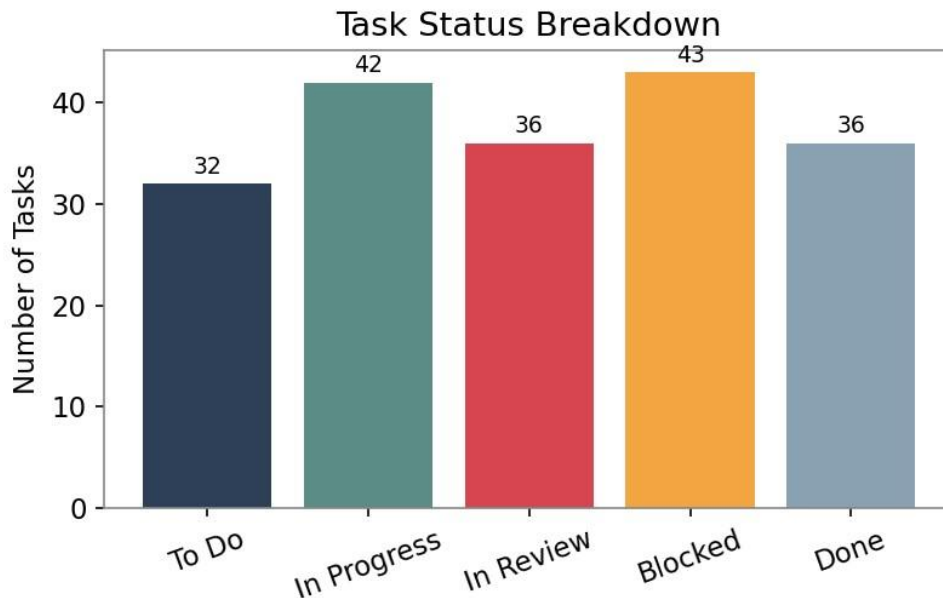


Blocked tasks (43) outnumber every other status, ahead of In Progress (42) and In Review (36). Only 36 of 189 tasks (19%) are Done. Estimated effort across all tasks totals 8,209 hours versus 7,205 actual hours logged — a net variance of -1,004 hours, suggesting estimation is reasonably close in aggregate even though individual tasks vary.

Milestone Delivery

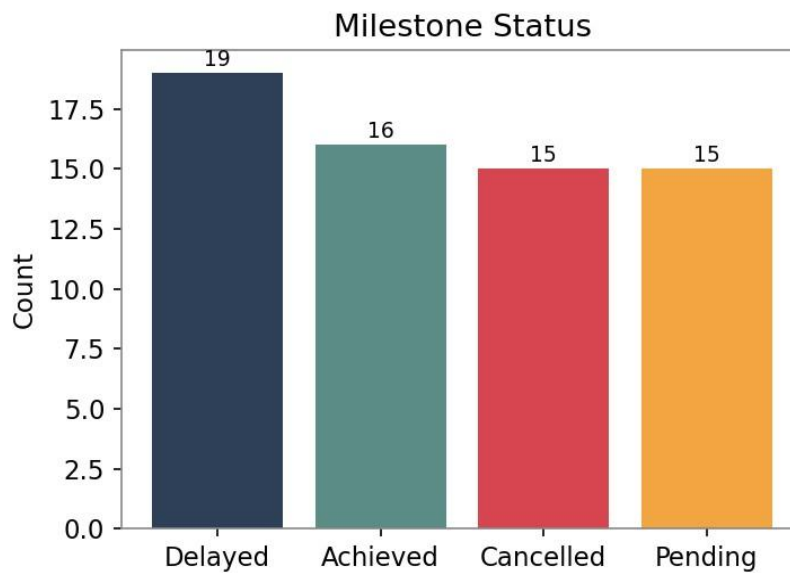

19 of 65 milestones (29%) are Delayed, roughly on par with the 16 Achieved — a signal that scheduling risk is systemic across the portfolio rather than isolated to one or two projects.

HR & Performance

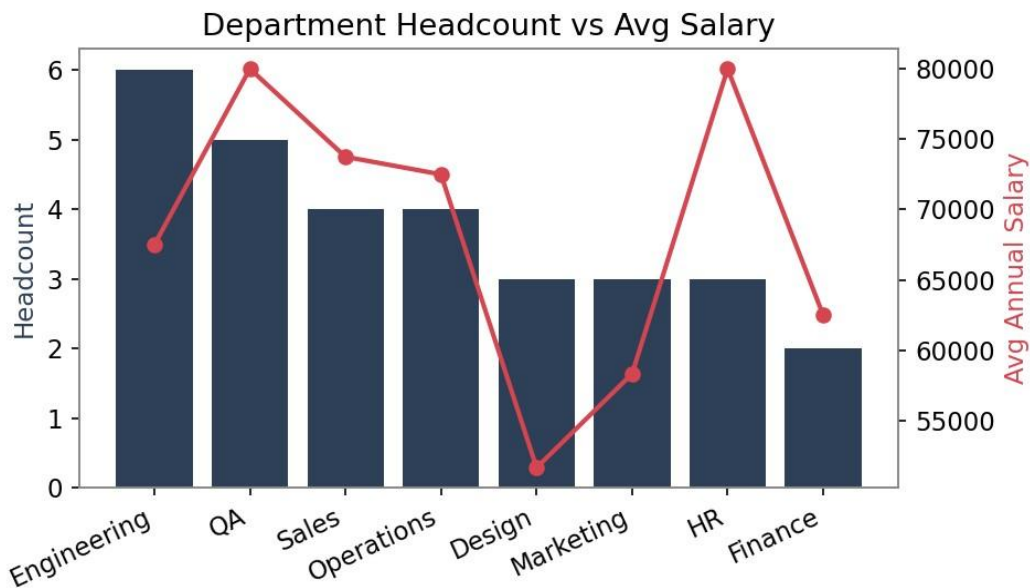

Engineering is the largest department (6 employees), while HR and QA carry the highest average annual salary (■80,000). 5 of 30 employees are currently Inactive.

Performance Ratings



Top 5 Performers (avg. score)

Employee	Department	Avg Score
Vikram Dubey	QA	4.70
Anjali Srivastava	Operations	4.45
Nitin Saxena	Finance	4.30
Karan Mishra	QA	4.25
Anjali Tiwari	Sales	4.20

Employees Needing Support (lowest avg. score)

Employee	Department	Avg Score
Ritu Gupta	Engineering	2.80
Shruti Verma	HR	2.85
Swati Saxena	HR	3.00
Rajesh Pandey	Marketing	3.05
Karan Pandey	Operations	3.05

Resourcing Risk: Over-allocated Employees

14 of 25 employees with active project assignments are allocated beyond 100% of capacity when their active assignments are summed — a likely contributor to the high Blocked-task count and Delayed-milestone rate seen earlier in this report.

Employee	Department	Total Allocation %
Aarav Saxena	Operations	371%
Pooja Verma	Engineering	314%
Karan Rastogi	QA	249%
Rajesh Pandey	Marketing	249%
Aarav Mehta	Design	211%
Suresh Chauhan	HR	204%
Pooja Singh	Engineering	197%
Nisha Singh	Sales	178%
Karan Mishra	QA	147%
Vivek Joshi	Operations	117%

Key Recommendations

- Prioritize unblocking tasks: 43 tasks are Blocked — identify and resolve the top blockers first, since this is the single largest task-status bucket.
- Re-baseline or re-scope the 7 On-Hold projects; carrying them without action inflates the portfolio's apparent size without contributing to delivery.
- Investigate the 2 over-budget projects (Marketing Campaign Program C, Security Audit Program A) before costs run further ahead of progress.
- Rebalance workload for the 14 over-allocated employees, starting with the top 5 (over 200% allocation), to reduce burnout risk and improve on-time delivery.
- Pair lower-scoring employees with development plans or mentoring, particularly where scores cluster below 3.0.
